



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering

Ref. No.: IIT(BHU)/CE/KrKP/25-26/UPRNSS/ITI/Chhanbe/Mirzapur/Rooms/02 Date: 14/11/2025

Third Party Inspection Report on Construction of Various Rooms in the Campus of ITI Chhanbe, Dist. Mirzapur (UP)

A. General

1	Reference letter no.	783/Work-190, Dated: 10/09/2025
2	Date of Inspection	5 th October, 2025
3	Name of Construction Agency	UPRNSS Ltd., Mirzapur
4	Name of Architect	UPRNSS, Lucknow
5	Name of Structural Consultant	ATS Structural Consultants, Lucknow
6	Name of the officials present during site inspection	Er. Deenanath Yadav, JE, UPRNSS, Mirzapur
7	Project Cost	Rs. 299.00 Lac
8	% progress of work at the time of inspection	95 %
9	Type of work	Framed structure

B. Detail of the site elements

1. Main building (G+1)
2. Boundary wall (130 rm)
3. Fire fighting work
4. CC Road

C. Progress of the work

Following is the progress of work-

Sr. No.	Elements	Progress	Completion
1	Main building (G+1)	Foundation (Isolated and combined) completed, Brick work completed, Slab work completed, Earthwork completed, Water	100 %

(Signature)



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering

		proofing work completed, Plastering and painting completed. Door & window work completed. Quality of work is as per the norms and found satisfactory.	
2	Boundary wall	Retaining wall cum boundary wall construction completed as per the norms. Work quality is satisfactory.	100 %
3	Fire fighting work	Completed as per the norms	100 %
4	CC Road	Work is in progress.	-
Overall Progress		95 %	

D. Material used

1	Concrete	M20 (1:1.5:3) (Nominal Mix)
2	Brick	150 class. Marka, Satya
3	Cement	Ultratech cements
4	Reinforcement	Kamdhenu Fe 500
5	Sand	Zone 2
6	Flooring	Kota
7	Railing	MS Railing

E. Routine quality control

1	Material testing report	Material testing reports are available at site.
2	Quality inspection	Regular inspection by PWD and other committees.
3	Vetted design and drawing details	Approved drawings are available at site.
4	Testing facilities at the site	Not available
5	Soil investigation report	Soil investigation reports are available at site.

F. Quality statement


The overall quality of the Construction of various rooms in the Campus of ITI Chhanbe, Dist. Mirzapur (UP) is found satisfactory. Inventory of the building is already submitted to the Principal, ITI Chhanbe on 26 Sept.2025.

Karun



भारतीय
प्रौद्योगिकी
संस्थान

काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering

G. Recommendations:

- Unfilled tile joints should be completed grouted.
- Column head on the terrace should be properly cast.
- Drain along the boundary wall should be properly laid.
- Signage should be placed on the building elements.
- Building should be properly cleaned before handover.

Prof. K.K. Pathak
Department of Civil Engineering
Indian Institute of Technology (BHU) Varanasi

Prof. K. K. PATHAK
Department of Civil Engineering
Indian Institute of Technology
Banaras Hindu University
Varanasi-221005



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering



Fig. 1: Front view of the building

Pranav Ch



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering

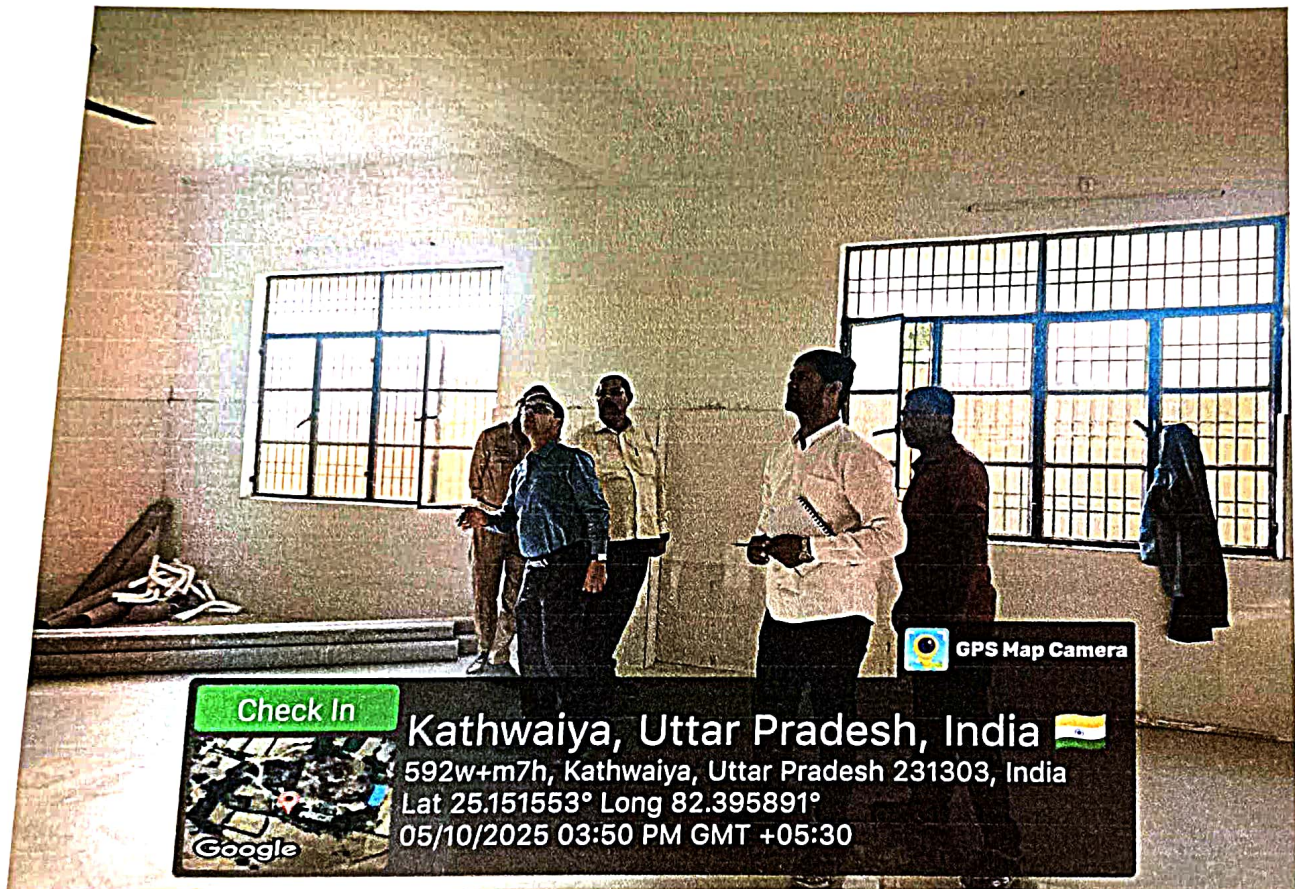


Fig. 2: Inspection of class room

10/10/2025



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering


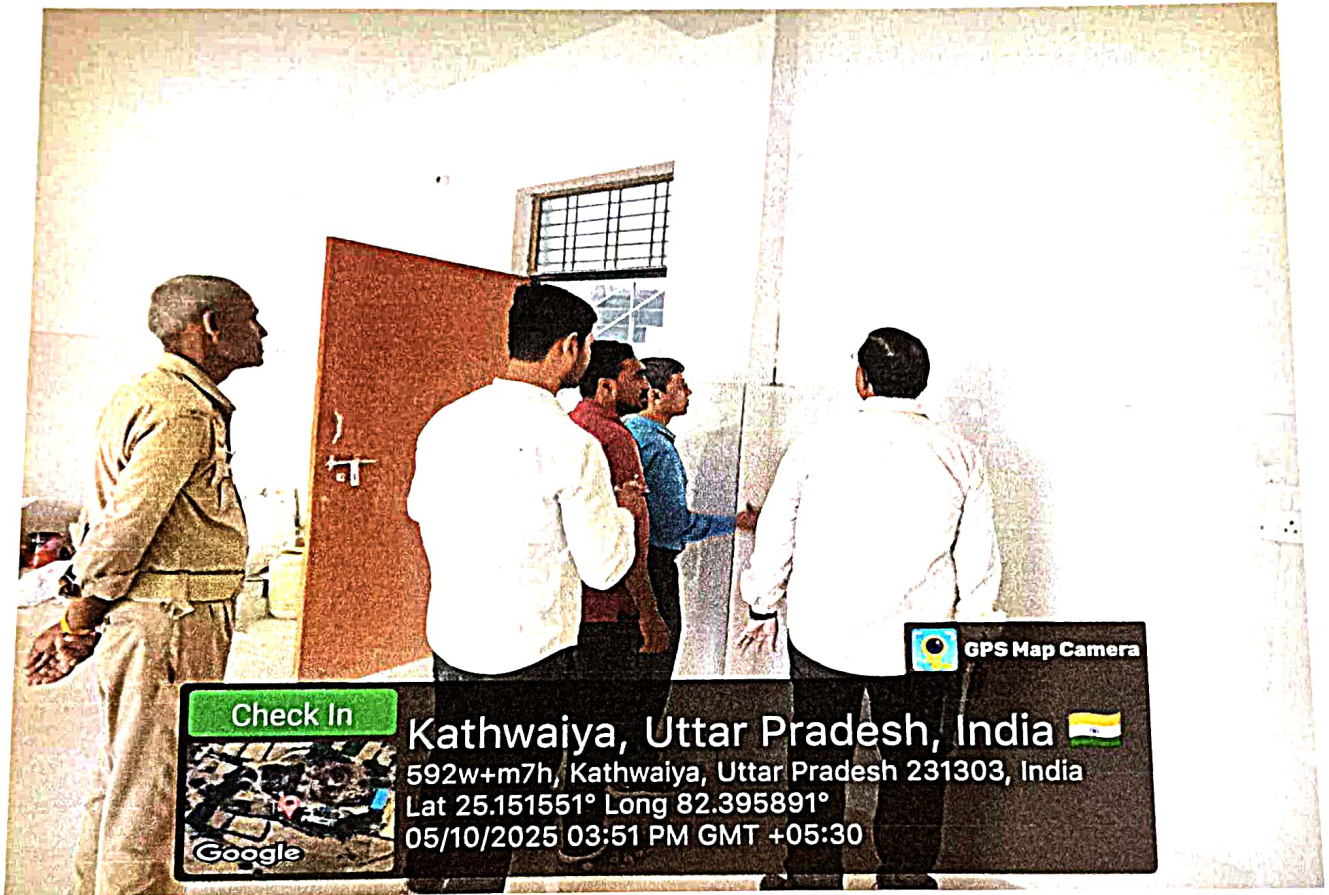


Fig. 3: Inspection of wall tiles

Pranav



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering



Fig. 4: Inspection of flooring

Kumar



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering



Fig. 5: Inspection of finishing work

10/10/2025



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering



Fig. 6: Inspection of staircase

Kumar



भारतीय
प्रौद्योगिकी
संस्थान
काशी हिन्दू विश्वविद्यालय



INDIAN
INSTITUTE OF
TECHNOLOGY
BANARAS HINDU UNIVERSITY

Department of Civil Engineering

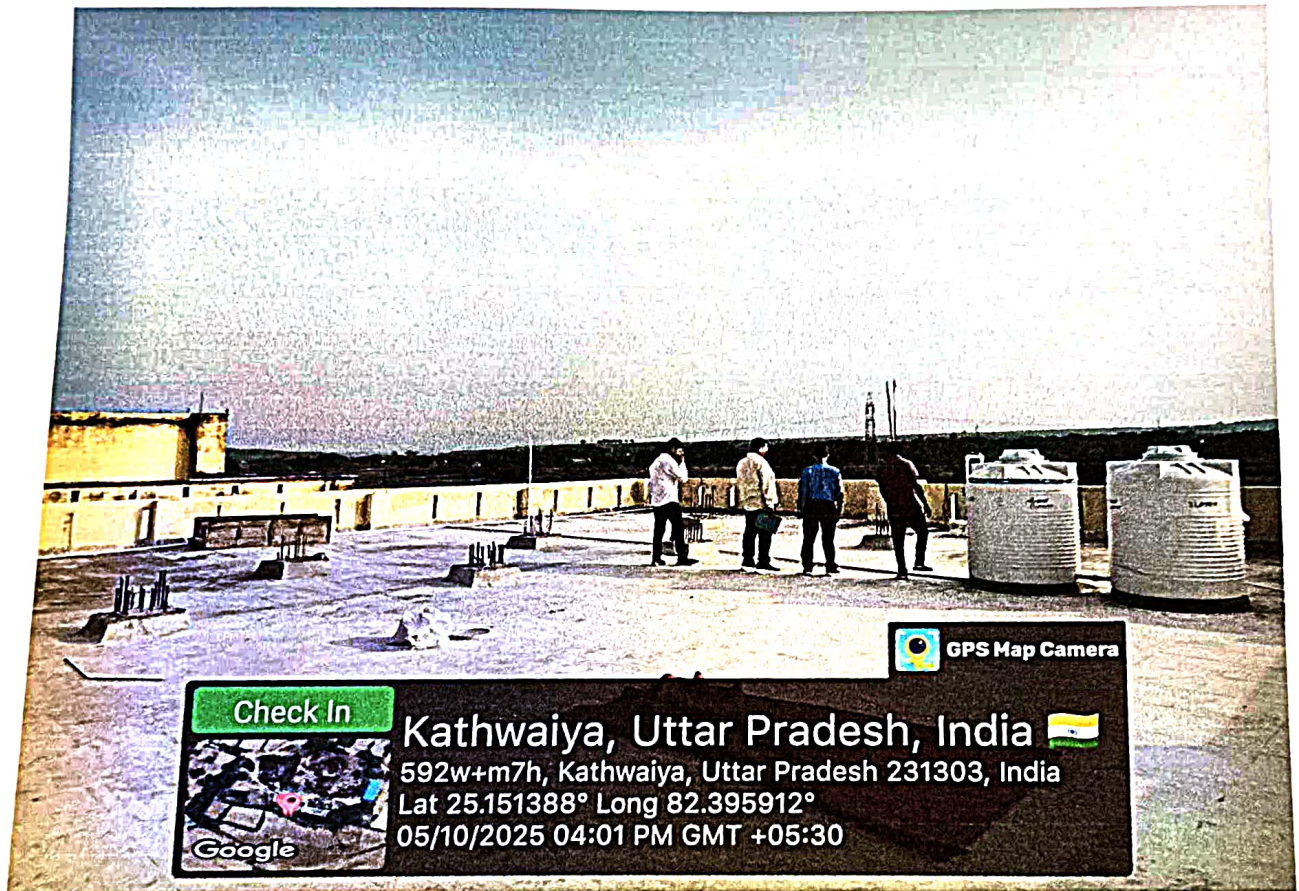


Fig. 7: Inspection of terrace

Kamran
