

THIRD PARTY QUALITY ASSURANCE REPORT
of
75 BEDDED GIRLS HOSTEL IN GOVERNMENT
VISUALLY IMPAIRED GIRLS SCHOOL,
RAMPUR MANIHARAN
DISTRICT SAHARANPUR

Submitted to

The Executive Engineer
U.P.R.N.S.S.
Saharanpur (U. P.)

by



Department of Civil Engineering
Z. H. College of Engineering & Technology
A.M.U., Aligarh
Aligarh

NOVEMBER 2025

Table of Contents

Sl. No.	Item	Page No.
i.	Certificate	3
ii.	Acknowledgement	4
1.	Introduction	5
2.	Description of Work	5
3.	Visual Inspection & Observations	5
4.	Non-Destructive Tests (NDT)	6
5.	Concluding Remarks	14
6.	Conclusion	15
7.	References	15
8.	Annexure-I Photographs	16-20
9.	Annexure-II Material Testing Reports	21-41


CERTIFICATE

We, hereby, certify that the **75 Bedded Girls Hostel in Government Visually Impaired Girls School, Rampur Maniharan, District Saharanpur (U. P.)** has been done personally by us and the matter presented in this third-party quality assurance report is true to the best of our knowledge. This report reflects the condition of structural members at the day of visit. This report is for quality monitoring purposes and not for legal or contractual claims.



(Prof. T. Naqvi)

Professor
Civil Engineering Department
A.M.U., Aligarh-202002



(Prof. M. S. Jafri)

Professor
Civil Engineering Department
A.M.U., Aligarh-202002

ACKNOWLEDGEMENT


The investigators place on record their appreciation to the team members of **U.P.R.N.S.S. Saharanpur (U. P.)** who extended all possible support during inspection of the work.

The cooperation received from all the other officers and staff members is also gratefully acknowledged.



(Prof. T. Naqvi)

Professor
Civil Engineering Department
A.M.U., Aligarh-202002



(Prof. M. S. Jafri)

Professor
Civil Engineering Department
A.M.U., Aligarh-202002

1. INTRODUCTION

With reference to Letter No 365/U.P.R.N.S.S./NIPRESS/2025-26 Dated 14.11.2025 from Executive Engineer, **U.P.R.N.S.S. Saharanpur (U. P.)**, the expert committee from the Department of Civil Engineering, A.M.U., Aligarh conducted the third-party quality inspection of **75 Bedded Girls Hostel in Government Visually Impaired Girls School, Rampur Maniharan, District Saharanpur (U. P.) on 25.11.2025.**

The expert committee carried out visual inspection followed by non-destructive tests of the building in presence of Resident Engineer Er. Pushpendra, Junior Engineer and representatives of contractor. The details of investigation, observations and comments are given in this report.

2. DESCRIPTION OF WORK

The proposed building is G+3 storeyed framed structure. Total proposed area of building is 2168 m² of which total ground floor and first floor area is 560 m². The area of second and third floor is 536sq m². There is provision of lift proposed. Structural system for building is combination of column with conventional beam-slab system. M25 Grade of concrete has been recommended by designer for use in beam, slab and columns. Construction work was started in May 2025. Only ground floor structural members were tested. Shuttering for the first floor slab was in place. It is clarified that technical review/evaluation of the structural design and drawings of the project is not a part of the scope of this report. The condition of foundation was not possible for visual inspection. Hence, could not be considered for inspection.

3. VISUAL INSPECTION AND OBSERVATIONS

The team started by visual inspection of structure followed by Non-Destructive Testing using Rebound Hammer and Ultrasonic Pulse Velocity (UPV) test. The expert committee carried out visual inspection and measurement of members. MTC (Material Testing Certificate) for material used in construction is satisfactory placed at Annexure II. The observations of expert committee are as follows:-

- No visible cracks or sign of distress were observed in Beams, Columns & Slabs.
- The surface finish of the concrete was found to be satisfactory and free from honeycombing or segregation.

- Slabs surfaces were found to be smooth and without sagging. Thus, structure is sound.
- Doors and windows are aligned correctly.
- Fair quality bricks have been used.


The observations made about members relate to only what could be randomly measured at different locations. Engineers and supervisory staff shall thoroughly inspect the entire work for any defects and take suitable remedial measures properly.

4. NON-DESTRUCTIVE TESTS (NDT)

After visual inspection, testing of different components of the building by Non-Destructive Tests (NDT) was started. As per the recommendations of the Indian Standard IS-15988:2013 “Seismic Evaluation and Strengthening”, the NDT test has been performed to test the quality of existing concrete. The Non-Destructive Tests (NDT) are now being considered powerful methods of evaluating the existing concrete structures with regard to their strength and durability. The use of NDT has gained momentum over the last few decades owing to the ease of operation. It can very well supplement the other findings for a reasonably good estimation of the strength of a deteriorated concrete in a distressed structure. The Schmidt Rebound Hammer Test (SRHT) is commonly used to determine the in-place quality and strength of concrete.

4.1 REBOUND HAMMER TEST

Rebound Hammer test measures the surface hardness of concrete with approximate correlations to estimate the compressive strength of the structure. Rebound Hammer tests are conducted in accordance with IS: 13311 Part II standard.

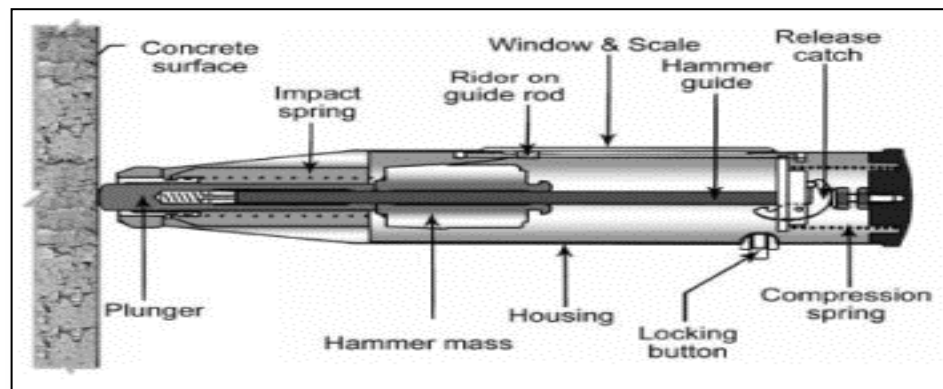

Objective

The rebound hammer method could be used for:

- ☐ assessing the likely compressive strength of concrete with the help of suitable correlations between rebound index and compressive strength,
- ☐ assessing the uniformity of concrete,
- ☐ assessing the quality of the concrete in relation to standard requirements, and
- ☐ assessing the quality of one element of concrete in relation to another.

Principle

When the plunger of rebound hammer is pressed against the surface of the concrete, the spring-controlled mass rebounds and the extent of such rebound depends upon the surface hardness of concrete. The surface hardness and therefore the rebound is taken to be related to the compressive strength of the concrete. The rebound is read off along a graduated scale and is designated as the rebound number or rebound index.

Interpretation of Results

The rebound hammer method provides a convenient and rapid indication of the compressive strength of concrete by means of establishing a suitable correlation between the rebound index and the compressive strength of concrete. In general, the rebound number increases as the strength increases but it is also affected by a number of parameters.

It is also pointed out that rebound indices are indicative of compressive strength of concrete to a limited depth from the surface. If the concrete in a particular member has internal micro-cracking, flaws or heterogeneity across the cross-section, rebound hammer indices will not indicate the same.

As such, the estimation of strength of concrete by rebound hammer method cannot be held to be very accurate and probable accuracy of prediction of concrete strength in a structure is ± 25 percent.

Table 1 given below shows the cube compressive strength of different components corresponding to their rebound numbers. The beams, columns and slabs were randomly selected out of critical members.

Table 1: Strength Evaluation by Schmidt Rebound Hammer Test (SRHT)

Location/ Grid	Element	Compressive Strength Based on Average of five Values of Rebound Numbers (MPa)	Design Strength
Ground Floor Grid 21/M	Column C10 (300×450mm ²)	27.66	M25
Ground Floor Grid 17/H	Column C13 (D= 400mm)	27.78	M25
Ground Floor Grid 19/G	Column C6 (350×750mm ²)	28.22	M25
Ground Floor Grid 20-21/L-M	Slab S1	30.4	M25
Ground Floor Grid 21/L-M	Beam B8 (230×450mm ²)	28.5	M25
Ground Floor Grid 19-21/M	Plinth Beam PB6 (230×450mm ²)	27.5	M25
Ground Floor Grid 17-20/G-L	Slab S1	30.6	M25
Ground Floor Grid 17-19/H	Beam B5 (230×450mm ²)	27.12	M25
Ground Floor Grid 17/G-L	Beam B5 (230×450mm ²)	26.76	M25
Ground Floor Grid 17-19/D	Beam B6 (230×450mm ²)	26.8	M25
Ground Floor Grid 17-19/B-G	Slab S1	35.4	M25
Ground Floor Grid 18/D-E	Beam B5 (230×450mm ²)	26.8	M25
Ground Floor Grid 18/B	Column C5 (400×600mm ²)	28.4	M25
Ground Floor Grid 17-20/A-B	Slab S2	30.5	M25
Ground Floor Grid 18-19/B	Beam B12 (230×450mm ²)	28.5	M25
Ground Floor Grid 18/A-B	Beam B1 (300×600mm ²)	27.5	M25
Ground Floor Grid 18-20/A	Beam B10 (300×600mm ²)	29.2	M25
Ground Floor Grid 20-21/A	Column C9 (400×600mm ²)	29.7	M25
Ground Floor Grid 17-20/A-B	Slab S2	30.6	M25
Ground Floor Grid 20/A-B	Beam B4 (230×450mm ²)	28.2	M25


Ground Floor Grid 10/D	Column C13 (D= 400mm)	29.7	M25
Ground Floor Grid 9-17/B-D	Slab S1	34.5	M25
Ground Floor Grid 10/B-D	Beam B6 (230×450mm ²)	27.8	M25
Ground Floor Grid 10-13/D	Beam B5 (230×450mm ²)	27.8	M25
Ground Floor Grid 8/A	Column C1 (400×750mm ²)	26.9	M25
Ground Floor Grid 8-12/A-B	Slab S1	36.8	M25
Ground Floor Grid 8/A-B	Beam B2 (300×600mm ²)	26.6	M25
Ground Floor Grid 8-12/A	Beam 10 (300×600mm ²)	29.2	M25
Ground Floor Grid 3-8/A-B	Plinth Beam PB2 (230×350mm ²)	27.5	M25
Ground Floor Grid 3/B	Column C4 (400×750mm ²)	27.3	M25
Ground Floor Grid 3-8/B-F	Slab S1	36.8	M25
Ground Floor Grid 3-/B	Beam B10 (300×600mm ²)	26.6	M25
Ground Floor Grid 3/B-E	Beam B3 (300×600mm ²)	26.9	M25
Ground Floor Grid 10/H	Column C13 (400×750mm ²)	28.2	M25
Ground Floor Grid 10/H-J	Plinth Beam PB7 (230×350mm ²)	27.8	M25
Ground Floor Grid 5/M	Column C3 (400×750mm ²)	28.6	M25
Ground Floor Grid 5-10/J-M	Slab S1	29.8	M25
Ground Floor Grid 5/J-M	Beam B10 (300×600mm ²)	27.7	M25
Ground Floor	Landing	28.6	M25

The results show that at all of the locations tested the compressive strength obtained for the in-situ concrete is **more than** designed characteristic strength of concrete. The tests are carried out in all types of structural elements including columns, beams and slabs. It is pertinent to mention that the Rebound Hammer Tests predict relative strength of concrete based on the hardness at or near exposed surfaces after applying appropriate correlation/correction factor. **Overall, the compressive strength values estimated from Rebound Hammer Tests are**

found to be satisfactory. However, the rebound hammer results are further co-related with the UPV results.

4.2 ULTRASONIC PULSE VELOCITY TEST (UPV) RESULTS

Ultrasonic Pulse Velocity (UPV) Test involves the transmission of ultrasonic pulses through the structural member and computing the wave velocity in it. Thus, computed velocity is an indicative of the quality of concrete and if the member is suffering from any structural flaw like honeycombing, voids etc. UPV tests are conducted according to IS: 13311- Part 1.

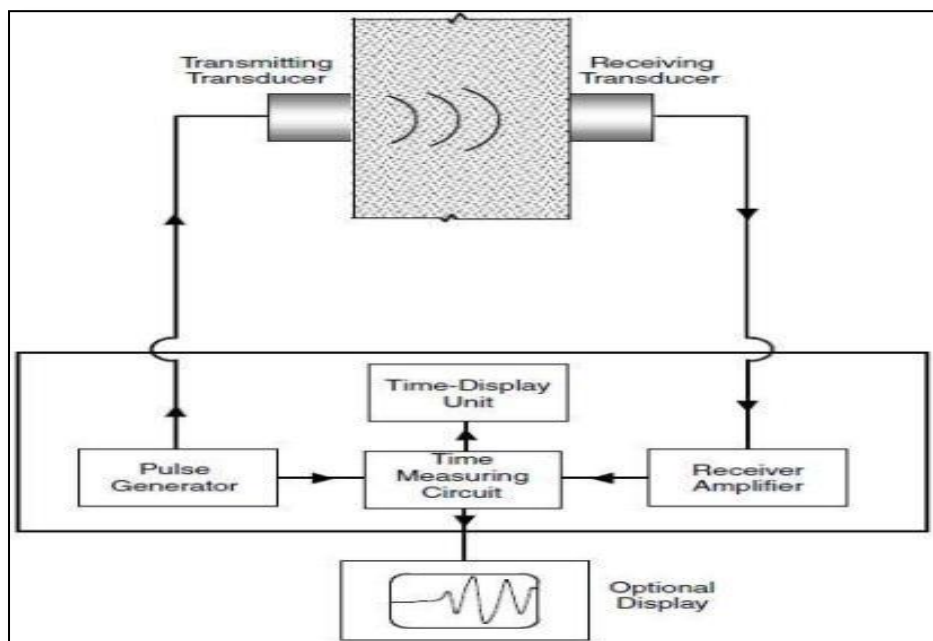

Object

The ultrasonic pulse velocity method could be used to establish:

- ☐ the homogeneity of the concrete,
- ☐ the presence of cracks, voids, and other imperfections,
- ☐ changes in the structure of the concrete which may occur with time,
- ☐ the quality of the concrete in relation to standard requirements,
- ☐ the quality of one element of concrete in relation to another.

Principle

The ultrasonic pulse is generated by an electro acoustical transducer. When the pulse is induced into the concrete from a transducer, it undergoes multiple reflections at the boundaries of the different material phases within the concrete. A complex system of stresswaves is developed which includes longitudinal (compressional), shear (transverse) and surface (Rayleigh) waves. The receiving transducer detects the onset of the longitudinal waves, which is the fastest.

Because the velocity of the pulses is almost independent of the geometry of the material through which they pass and depends only on its elastic properties, pulse velocity method is a convenient technique for investigating structural concrete.

The underlying principle of assessing the quality of concrete is that comparatively higher velocities are obtained when the quality of concrete in terms of density, homogeneity and uniformity is good. In case of poorer quality, lower velocities are obtained. If there is a crack, void or flaw inside the concrete which comes in the way of transmission of the pulses, the pulse strength is attenuated and it passes around the discontinuity, thereby making the path length longer. Consequently, lower velocities are obtained. The actual pulse velocity obtained depends primarily upon the materials and mix proportions of concrete. Density and modulus of elasticity of aggregate also significantly affect the pulse velocity.

Interpretation of Results

The ultrasonic pulse velocity of concrete is mainly related to its density and modulus of elasticity. This in turn, depends upon the materials and mix proportions used in making concrete as well as the method of placing, compaction and curing of concrete.

For example, if the concrete is not compacted as thoroughly as possible, or if there is segregation of concrete during placing or there are internal cracks or flaws, the pulse velocity will be lower, although the same materials and mix proportions are used.

The quality of concrete in terms of uniformity, incidence or absence of internal flaws, cracks and segregation, etc, indicative of the level of workmanship employed; can thus be assessed using the guidelines given in Table 2, which have been evolved for characterizing the quality of concrete in structures in terms of the ultrasonic pulse velocity.

**Table 2: Velocity Criterion for Concrete Quality Grading (Clause 2.5.2) of
IS: 516 (Part 5/Sec 1): 2018 (Amendment No 1 Dated November 2019).**

UPV Value in km/sec (V)	Concrete Quality
For Concrete ($\leq$M25)	
V above 4.5	Excellent
V between 3.5 and 4.5	Good
V below 3.5	Doubtful
For Concrete ($>$M25)	
V above 4.5	Excellent
V between 3.75 and 4.5	Good
V below 3.75	Doubtful

Since actual values of the pulse velocity obtained, depend on a number of parameters, any criterion for assessing the quality of concrete on the basis of pulse velocity as given in Table 2 can be held as satisfactory only to a general extent. However, when the comparison is made amongst different parts of a structure, which have been built at the same time with supposedly similar materials, construction practices and supervision, the assessment of quality becomes more meaningful and reliable.

The assessment of compressive strength of concrete from ultrasonic pulse velocity values is not adequate because the statistical confidence of the correlation between ultrasonic pulse velocity and the compressive strength of concrete is not very high. The reason is that a large number of parameters are involved, which influence the pulse velocity and compressive strength of concrete to different extents. However, if actual concrete materials and mix proportions adopted in a particular structure are available, then estimate of concrete strength can be made by establishing suitable correlation between the pulse velocity and the compressive strength of concrete specimens made with such materials and mix proportions, under environmental conditions similar to that in the structure. The estimated strength may vary from the actual strength by 20 percent. The correlation so obtained may not be applicable for concrete of another grade or made with different types of materials.

Table 3 gives an estimate of quality of concrete using PUNDIT. The experiment's specific equipment determines the travel time of an ultrasonic wave through the concrete member between the transmitter and receiver placed on two opposite/ same sides of the sample.

Table 3 Quality by Ultrasonic Pulse Velocity Test (PUNDIT)

Test No.	Location	Type of Element	Speed (km/Ground)	Quality of Concrete
1.	Ground Floor Grid 21/M	Column C10 (300×450mm ²)	4.23	Good
2.	Ground Floor Grid 17/H	Column C13 (D= 400mm)	4.03	Good
3.	Ground Floor Grid 19/G	Column C6 (350×750mm ²)	4.27	Good
4.	Ground Floor Grid 8/A	Column C1 (400×750mm ²)	4.12	Good
5.	Ground Floor Grid 10/H	Column C13 (400×750mm ²)	4.11	Good
6.	Ground Floor Grid 10/H-J	Plinth Beam PB7 (230×350mm ²)	4.24	Good
7.	Ground Floor Grid 5/M	Column C3 (400×750mm ²)	4.03	Good
8.	Ground Floor Grid 17-20/A-B	Slab S2 (indirect method)	4.22	Good
9.	Ground Floor Grid 18-19/B	Beam B12 (230×450mm ²)	4.08	Good
10.	Ground Floor Grid 18/A-B	Beam B1 (300×600mm ²)	4.11	Good
11.	Ground Floor Grid X25-X28/Y16	Beam B38 (300×600mm ²)	4.45	Good
12.	Ground Floor Grid X23/Y16-Y17	Beam B43 (300×600mm ²)	4.21	Good

The pulse velocity test results obtained were evaluated as per IS 516 (Part 5/ Sec 1):2018 (Amendment No 1 Dated November 2019). Very consistent results of UPV Tests are obtained and at all locations, the concrete quality grading is in the range of "GOOD". It may be noted that due to construction of partition walls and from accessibility considerations, the tests could be carried out by the in-direct transmission method. In- direct transmission, i.e., surface probing in general gives lower pulse velocity than the direct transmission method, i.e., cross probing. As

per clause 2.4.3.2.5 of IS 516 (Part 5/ Sec 1): 2018 the obtained pulse velocities have to be enhanced by 0.5 km/sec, same has been done in above readings. Overall, the UPV tests show that concrete along the structural members is consistent and uniform, and in general the quality of concrete in structural members is acceptable. **The UPV test results for the Building are good in terms of concrete quality (concrete soundness).**

5. CONCLUDING REMARKS

1. The quality of Civil construction works tested by non-destructive methods was found to be satisfactory.
2. Construction work is under progress.
3. All Columns, Beams and Slabs as observed by visual inspection have been found in a good condition as can be seen in Figures too. No sign of distress has been seen in any of the columns.
4. For the Columns, Beams and Slabs the compressive strength is more than design strength at all locations where test was performed hence the work is satisfactory.
5. The results of the Non-Destructive Test through PUNDIT further validate that the strength of RCC members is satisfactory.
6. The condition of foundation was not possible for visual inspection. Hence, could not be considered for inspection.
7. The Engineers and Contractor were given verbal tips how to maintain quality during construction.
8. This is only the expert opinion based on certain tests performed at sites and certain statistical data analysed to verify the test results. The results are found to be satisfactory.
9. This report is for quality monitoring purposes and not for legal or contractual claims.
10. Some of the photographs taken from the site during inspection/testing are placed at Annexure I.
11. The total report comprises of 15 pages excluding Annexure.

6. CONCLUSION

Based on the NDT test results and visual inspection of the **75 Bedded Girls Hostel in Government Visually Impaired Girls School, Rampur Maniharan, District Saharanpur (U.P.)** it is observed that the general condition of the construction is **satisfactory**. The expert team is satisfied with the quality of construction work.

7. REFERENCES

1. Concrete Microstructure, Properties and Materials- P.K. Mehta Paulo and J.M.Monterio, 1999.
2. Guide to Durable Concrete - ACI Committee 201 Report, ACI Journal, Dec. 1977.
3. IS:456 (2000)- Code of Practice for Plain and Reinforced Concrete, BIS, New Delhi.
4. IS:13311 (Part 1):1992 Non-destructive Testing of Concrete – Methods of Test [Part 1ULTRASONIC PULSE VELOCITY]
5. IS:13311 (Part 2):1992 Non-destructive Testing of Concrete – Methods of Test [Part 2REBOUND HAMMER TEST]

(Prof. T. Naqvi)

Professor
Civil Engineering Department
A.M.U., Aligarh-202002

(Prof. M. S. Jafri)

Professor
Civil Engineering Department
A.M.U., Aligarh-202002

8. Annexure-I: Photographs



Site



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test



Rebound hammer test




Rebound hammer test



Rebound hammer test

		
Rebound hammer test	Rebound hammer test	Team at site


(Prof. T. Naqvi)
 Professor
 Civil Engineering Department
 A.M.U., Aligarh-202002


(Prof. M. S. Jafri)
 Professor
 Civil Engineering Department
 A.M.U., Aligarh-202002

9. Annexure-II Material Testing Reports



कार्यालय अधिशासी अभियन्ता,
प्रान्तीय खण्ड, लोक निर्माण विभाग, सहारनपुर
Office of Executive Engineer, Provincial Division, PWD, Saharanpur
Email: pdpwsre@gmail.com



पत्रांक 5958 / T1 - प्रयोगशाला

सेवा में,

दिनांक 18-7-25

विषय:- प्रयोगशाला परीक्षण परीणाम

संदर्भ:- आपका पत्रांक:- 155/अधी०अधी०ए०ए०निप्रस/2526 व 01-7-25

महोदय,

उपरोक्त संदर्भ में आपके द्वारा कार्यालय अधिशासी अभियन्ता, प्रान्तीय खण्ड, लो०नि०वि०, सहारनपुर में जमा किये गये परीक्षण शुल्क हेतु रसीद नं० 869885 दिनांक 11-7-25 रू० 2298/- है।

कार्य का नाम: स्पेशल ब्रिक्स द्वारा निर्माणित कोलका विद्यालय, शुभपुर, मोनहारन

जनपद सहायक में 75 केस कोलका द्वारा वास का निर्माण कार्य

नमूना परीक्षण परीणाम:

S. No.	Type of Sample & Mark	Compressive Strength in N/mm ²	Average In N/mm ²	Permissible Limit	
				Code IS 1077:1992	
1	इटेम 1 (गठन)	16.23	15.90	30 25 20 17.5 15 12.5 10	Individual & Average Compressive Strength in N/mm ² Not Less than 30.0 25.0 20.0 17.5 15.0 12.5 10.0
2	4	16.30			
3	4	15.58			
4	4	16.02			
5	4	15.37			

S. No.	Sample	Date of Casting	Date of Testing	Compressive Strength in N/mm ²	Average In N/mm ²	Permissible Limit
1	C.C. Cube M-25	28-5-25	07-7-25	26.09	26.80	Code IS 456:2000 1-Specified - Individual test Grade - Result in N/mm ² M15- $\geq F_{ck}-3$ N/mm ² M20 For Above $\geq F_{ck}-4$ N/mm ² Individual variation $\pm 15\%$ of average compressive Strength
2	4	28-5-25	07-7-25	26.76		
3	4	28-5-25	07-7-25	27.56		

नोट: उपरोक्त परीक्षण के आंकड़े केवल आपके द्वारा उपलब्ध कराये गये नमूनों के लिये ही मान्य हैं।

प्रमुख अधिकारी प्रयोगशाला /
सहायक अभियन्ता
प्रान्तीय खण्ड लो०नि०वि०
सहारनपुर

G:\mangal kumar\mangal\2020-21

NAME of WORK = CONSTRUCTION of 75 BEDDED
for Disipibadhi HOSTEL AT Rampur Maniharan.
Sahasraipur.

Try. Form No. 385

(P)

RECEIPT FOR PAYMENT TO GOVERNMENT

(Form No. 1, Chapter III, Paragraph 26, Financial

Hand-book Volume V, Part I)

869885

Receipt No.

Date

Place RE

Department and Office

Received from
the sum of Rupees

on account of

Cashier or Accountant

सहायक अभियंता डी.पी. मारन पट्ट
डि.पी. मारन / दिनांक 1.7.25
दो हजार दो सौ अठानवे मात्र
रु. 1140/3

Signature of Government Servant
granting the receipt.

Designation



+91-9717912735

HS LABS PVT. LTD.


An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,

TEST REPORT

Report No.	HSL250807:20	Discipline :	Mechanical Testing	Page 1 to 2
Sample Type	TMT Steel -08mm	Group :	Mechanical Properties of Metal	
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Make :	Rathi	
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Grade :	Fe- 550D	
Agreement No.	--	Letter Date:	07/08/2025	
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Sample Receipt Date	07/08/2025	
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	Start Date of Analysis	08/08/2025	
Any Other Information	--	End Date of Analysis	14/08/2025	
		Date of Report Issue	14/08/2025	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
PHYSICAL PROPERTIES					
1	Tensile Strength	N/mm ²	710	600.0 Min.	IS: 1608(Pt-1)-2022
2	Elongation, on gauge length 5.65 vA where A is the cross section area of the test Piece	%	25.9	14.5 Min.	IS: 1608(Pt-1)-2022
3	Yield Stress	N/mm ²	614	550.0 Min.	IS: 1608(Pt-1)-2022
4	TS/YS Ratio	--	1.16	≥1.08	IS: 1608(Pt-1)-2022
5	Bend Test	--	Passes the test	There shall no rupture or cracks visible on the bent portion.	IS: 1599-2019
6	Re Bend Test	--	Passes the test	There shall no rupture or cracks visible on the Re bent portion.	IS: 1786-2008
7	Mass per meter	Kg/m	0.395	0.395±7%	IS: 1786-2008



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



+91-9717912735

HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,


TEST REPORT

Report No.	HSL250807:20	Discipline :	Chemical Testing	Page 2 to 2
Sample Type	TMT Steel -08mm	Group :	Metal & Alloys	
		Make :	Rathi	
		Grade :	Fe- 550D	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
CHEMICAL PROPERTIES					
1	Carbon	%	0.22	0.25 Max.	IS: 228 (Pt-1) -1987
2	Sulphur	%	0.026	0.040 Max.	IS: 228 (Pt-9) -1989
3	Phosphorus	%	0.029	0.040 Max.	IS: 228 (Pt-3) -2024
4	Sulphur + Phosphorus	%	0.055	0.075 Max.	IS: 228 (Pt-9 & 3)

Statement of conformity as per lab decision rules: The sample conforms to IS:1786-2008, Grade Fe-550D w.r.to the above tests.

End of Report






ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**

Report No.	HSL250807:21	Discipline :	Mechanical Testing	Page 1 to 2
Sample Type	TMT Steel -10mm	Group :	Mechanical Properties of Metal	
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Make :	Rathi	
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Grade :	Fe- 550D	
Agreement No.	--	Letter Date:	07/08/2025	
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Sample Receipt Date	07/08/2025	
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	Start Date of Analysis	08/08/2025	
Any Other Information	--	End Date of Analysis	14/08/2025	
		Date of Report Issue	14/08/2025	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
PHYSICAL PROPERTIES					
1	Tensile Strength	N/mm ²	722	600.0 Min.	IS: 1608(Pt-1)-2022
2	Elongation, on gauge length 5.65 VA where A is the cross section area of the test Piece	%	24.5	14.5 Min.	IS: 1608(Pt-1)-2022
3	Yield Stress	N/mm ²	613	550.0 Min.	IS: 1608(Pt-1)-2022
4	TS/YS Ratio	--	1.18	≥1.08	IS: 1608(Pt-1)-2022
5	Bend Test	--	Passes the test	There shall no rupture or cracks visible on the bent portion.	IS: 1599-2019
6	Re Bend Test	--	Passes the test	There shall no rupture or cracks visible on the Re bent portion.	IS: 1786-2008
7	Mass per meter	Kg/m	0.618	0.617±7%	IS: 1786-2008



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory, 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdiwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,


TEST REPORT

Report No.	HSL250807:21	Discipline :	Chemical Testing	Page 2 to 2
Sample Type	TMT Steel -10mm	Group :	Metal & Alloys	
		Make :	Rathi	
		Grade :	Fe- 550D	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
CHEMICAL PROPERTIES					
1	Carbon	%	0.23	0.25 Max.	IS: 228 (Pt-1) -1987
2	Sulphur	%	0.028	0.040 Max.	IS: 228 (Pt-9) -1989
3	Phosphorus	%	0.021	0.040 Max.	IS: 228 (Pt-3) -2024
4	Sulphur + Phosphorus	%	0.049	0.075 Max.	IS: 228 (Pt-9 & 3)

Statement of conformity as per lab decision rules: The sample conforms to IS:1786-2008, Grade Fe-550D w.r. to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7.




ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9335465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**

Report No.	HSL250807:22	Discipline :	Mechanical Testing	Page 1 to 2
Sample Type	TMT Steel -12mm	Group :	Mechanical Properties of Metal	
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Make :	Rathi	
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Grade :	Fe- 550D	
Agreement No.	--	Letter Date:	07/08/2025	
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Sample Receipt Date	07/08/2025	
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	Start Date of Analysis	08/08/2025	
Any Other Information	--	End Date of Analysis	14/08/2025	
		Date of Report Issue	14/08/2025	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
PHYSICAL PROPERTIES					
1	Tensile Strength	N/mm ²	699	600.0 Min.	IS: 1608(Pt-1)-2022
2	Elongation, on gauge length 5.65 VA where A is the cross section area of the test Piece	%	28.4	14.5 Min.	IS: 1608(Pt-1)-2022
3	Yield Stress	N/mm ²	590	550.0 Min.	IS: 1608(Pt-1)-2022
4	TS/YS Ratio	--	1.18	≥1.08	IS: 1608(Pt-1)-2022
5	Bend Test	--	Passes the test	There shall no rupture or cracks visible on the bent portion.	IS: 1599-2019
6	Re Bend Test	--	Passes the test	There shall no rupture or cracks visible on the Re bent portion.	IS: 1786-2008
7	Mass per meter	Kg/m	0.885	0.888±5%	IS: 1786-2008



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory, 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company

(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,

TEST REPORT

Report No.	HSL250807:22	Discipline :	Chemical Testing
Sample Type	TMT Steel -12mm	Group :	Metal & Alloys
		Make :	Rathi
		Grade :	Fe- 550D

Page 2 to 2

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
CHEMICAL PROPERTIES					
1	Carbon	%	0.24	0.25 Max.	IS: 228 (Pt-1) -1987
2	Sulphur	%	0.033	0.040 Max.	IS: 228 (Pt-9) -1989
3	Phosphorus	%	0.030	0.040 Max.	IS: 228 (Pt-3) -2024
4	Sulphur + Phosphorus	%	0.063	0.075 Max.	IS: 228 (Pt-9 & 3)

Statement of conformity as per lab decision rules: The sample conforms to IS:1786-2008, Grade Fe-550D w.r.to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**

Report No.	HSL250807:23	Discipline :	Mechanical Testing	Page 1 to 2
Sample Type	TMT Steel -16mm	Group :	Mechanical Properties of Metal	
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Make :	Rathi	
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Grade :	Fe-550D	
Agreement No.	--	Letter Date:	07/08/2025	
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Sample Receipt Date	07/08/2025	
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	Start Date of Analysis	08/08/2025	
Any Other Information	--	End Date of Analysis	14/08/2025	
		Date of Report Issue	14/08/2025	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
PHYSICAL PROPERTIES					
1	Tensile Strength	N/mm ²	709	600.0 Min.	IS: 1608(Pt-1)-2022
2	Elongation, on gauge length 5.65 VA where A is the cross section area of the test Piece	%	23.5	14.5 Min.	IS: 1608(Pt-1)-2022
3	Yield Stress	N/mm ²	596	550.0 Min.	IS: 1608(Pt-1)-2022
4	TS/YS Ratio	--	1.19	≥1.08	IS: 1608(Pt-1)-2022
5	Bend Test	--	Passes the test	There shall no rupture or cracks visible on the bent portion.	IS: 1599-2019
6	Re Bend Test	--	Passes the test	There shall no rupture or cracks visible on the Re bent portion.	IS: 1786-2008
7	Mass per meter	Kg/m	1.58	1.58 ± 5%	IS: 1786-2008



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001: 2015

+91-9717912735
HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,

TEST REPORT


Page 2 to 2

Report No.	HSL250807:23	Discipline :	Chemical Testing
Sample Type	TMT Steel -16mm	Group :	Metal & Alloys
		Make :	Rathi
		Grade :	Fe- 550D

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
CHEMICAL PROPERTIES					
1	Carbon	%	0.20	0.25 Max.	IS: 228 (Pt-1) -1987
2	Sulphur	%	0.024	0.040 Max.	IS: 228 (Pt-9) -1989
3	Phosphorus	%	0.029	0.040 Max.	IS: 228 (Pt-3) -2024
4	Sulphur + Phosphorus	%	0.053	0.075 Max.	IS: 228 (Pt-9 & 3)

Statement of conformity as per lab decision rules: The sample conforms to IS:1786-2008, Grade Fe-550D w.r.to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**

Report No.	HSL250807:24	Discipline :	Mechanical Testing	Page 1 to 2
Sample Type	TMT Steel -20mm	Group :	Mechanical Properties of Metal	
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Make :	Rathi	
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Grade :	Fe- 550D	
Agreement No.	--	Letter Date:	07/08/2025	
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Sample Receipt Date	07/08/2025	
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	Start Date of Analysis	08/08/2025	
Any Other Information	--	End Date of Analysis	14/08/2025	
		Date of Report issue	14/08/2025	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
PHYSICAL PROPERTIES					
1	Tensile Strength	N/mm ²	695	600.0 Min.	IS: 1608(Pt-1)-2022
2	Elongation, on gauge length 5.65 vA where A is the cross section area of the test Piece	%	22.5	14.5 Min.	IS: 1608(Pt-1)-2022
3	Yield Stress	N/mm ²	596	550.0 Min.	IS: 1608(Pt-1)-2022
4	TS/YS Ratio	--	1.17	≥1.08	IS: 1608(Pt-1)-2022
5	Bend Test	--	Passes the test	There shall no rupture or cracks visible on the bent portion.	IS: 1599-2019
6	Re Bend Test	--	Passes the test	There shall no rupture or cracks visible on the Re bent portion.	IS: 1786-2008
7	Mass per meter	Kg/m	2.46	2.47±3%	IS: 1786-2008



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,


TEST REPORT

Report No.	HSL250807:24	Discipline :	Chemical Testing	Page 2 to 2
Sample Type	TMT Steel -20mm	Group :	Metal & Alloys	
		Make :	Rathi	
		Grade :	Fe- 550D	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
CHEMICAL PROPERTIES					
1	Carbon	%	0.25	0.25 Max.	IS: 228 (Pt-1) -1987
2	Sulphur	%	0.031	0.040 Max.	IS: 228 (Pt-9) -1989
3	Phosphorus	%	0.035	0.040 Max.	IS: 228 (Pt-3) -2024
4	Sulphur + Phosphorus	%	0.066	0.075 Max.	IS: 228 (Pt-9 & 3)

Statement of conformity as per lab decision rules: The sample conforms to IS:1786-2008, Grade Fe-550D w.r.to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory, 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation, 3. Samples tested are Non-Returnable until specified at time of sample submission, 4. This report will not be valid for judicial purpose, 5. Total liability of our test house is limited to invoiced amount, 6. Result relate only to the item tested, 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company


(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (U.P.)-201007
 Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
 Piche Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,

TEST REPORT

Report No.	HSL250807:25	Discipline :	Mechanical Testing	Page 1 to 2
Sample Type	TMT Steel -25mm	Group :	Mechanical Properties of Metal	
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Make :	Rathi	
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Grade :	Fe- 550D	
Agreement No.	--	Letter Date:	07/08/2025	
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Sample Receipt Date	07/08/2025	
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	Start Date of Analysis	08/08/2025	
Any Other Information	--	End Date of Analysis	14/08/2025	
		Date of Report Issue	14/08/2025	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
PHYSICAL PROPERTIES					
1	Tensile Strength	N/mm ²	710	600.0 Min.	IS: 1608(Pt-1)-2022
2	Elongation, on gauge length 5.65 vA where A is the cross section area of the test Piece	%	21.8	14.5 Min.	IS: 1608(Pt-1)-2022
3	Yield Stress	N/mm ²	616	550.0 Min.	IS: 1608(Pt-1)-2022
4	TS/YS Ratio	--	1.15	≥1.08	IS: 1608(Pt-1)-2022
5	Bend Test	--	Passes the test	There shall no rupture or cracks visible on the bent portion.	IS: 1599-2019
6	Re Bend Test	--	Passes the test	There shall no rupture or cracks visible on the Re bent portion.	IS: 1786-2008
7	Mass per meter	Kg/m	3.83	3.85±3%	IS: 1786-2008



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



+91-9717912735
HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwari, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,


TEST REPORT

Report No.	HSL250807:25	Discipline :	Chemical Testing	Page 2 to 2
Sample Type	TMT Steel -25mm	Group :	Metal & Alloys	
		Make :	Rathi	
		Grade :	Fe- 550D	

Sr. No.	Test Parameters/ Characteristics	Units of Measurements	Results	Requirement as per IS: 1786-2008, Grade Fe-550D	Method Reference
CHEMICAL PROPERTIES					
1	Carbon	%	0.23	0.25 Max.	IS: 228 (Pt-1) -1987
2	Sulphur	%	0.028	0.040 Max.	IS: 228 (Pt-9) -1989
3	Phosphorus	%	0.031	0.040 Max.	IS: 228 (Pt-3) -2024
4	Sulphur + Phosphorus	%	0.059	0.075 Max.	IS: 228 (Pt-9 & 3)

Statement of conformity as per lab decision rules: The sample conforms to IS:1786-2008, Grade Fe-550D w.r.to the above tests.

****End of Report****



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory, 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation, 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.




+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**

Page 1 to 3

Report No.	HSL250807:26	Discipline :	Mechanical Testing
Sample Type	Design Mix	Group :	Building Material
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Grade :	M-25
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Letter Date:	07/08/2025
Agreement/Acceptance No.	--	Sample Receipt Date	07/08/2025
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Start Date of Analysis	08/08/2025
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	End Date of Analysis	18/08/2025
Any Other Information	--	Date of Report Issue	18/08/2025

1	Design Stipulation	
i.	Mean characteristics Strength at 28 days	25.0 N/mm ²
ii.	Degree of Quality control	Good
iii.	Maximum size of Aggregate	20.0 mm
iv.	Workability/Slump	75 - 100 mm
2	Test Data for Material	
i.	Cement (O.P.C Grade-43, Make-J.K. Super Cement)	
(a).	Compressive Strength (N/mm ²)	
a-i	3 days	28.0 N/mm ²
a-ii	7 days	39.7 N/mm ²
(b).	Density of Cement (gm/cc)	3.15
(c).	Density of Admixture (gm/cc)	1.10



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.

+91-9717912735



ISO 9001: 2015

HS LABS PVT. LTD.

+91-9717912735

An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delfhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,

TEST REPORT

Report No.	HSL250807:26	Discipline : Mechanical Testing	Page 2 to 3
Sample Type	Design Mix	Group : Building Material	
		Grade : M-25	

(d).	Aggregate					
d-i.	Specific Gravity	Coarse	Fine/Sand	Water		
d-ii.	Water Absorption %	2.70	2.61	1		
	Sieve Analysis	0.54	1.24	--		
		% Passing				
	Sieve Size	20mm	10mm	Combine Aggregate	Specified Value as per IS:383-2016	Requirement as per IS: 383-2016
		A	B	A : B	% Passing	
	40mm	100	100	60 : 40		
(e).	20mm	96.5	100	100	100	
	10mm	4.0	94.3	97.90	90-100	
	4.75mm	0.6	5.2	40.12	25-55	100
	2.36mm			2.44	0-10	100
	1.18mm					95.0
	0.6mm					82.2
	0.3mm					61.6
	0.15mm					41.2
						24.6
						7.2
						0 - 10
3	Target mean Strength (IS:456)	Zone-II				
4	Selection of water cement Ratio: As per the Target mean strength, compressive strength of cement and with reference to IS:456-2000, Water Cement Ratio	31.6 N/mm ²				
5	Water Content: As per the design stipulation water content	0.45				
6	Selection of cement content	162.9 Kg/m ³				
	Selection of Aggregate: As per the workability and quality of Aggregates	362 Kg/m ³				
	Fine Aggregate Content by mass					
7	Coarse Aggregate (Total) by mass	688 Kg/m ³				
	20mm Aggregate by mass	1211 Kg/m ³				
	10mm Aggregate by mass	727 Kg/m ³				
		484 Kg/m ³				



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.

the date
ssion. 4.
ested. 7



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.

An ISO 9001:2015 Certified Company

(A Govt. Approved Laboratory)

Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (UP)-201007
 Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
 Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,

TEST REPORT

Page 3 to 3


Report No.	HSL250807:26	Discipline : Mechanical Testing
Sample Type	Design Mix	Group : Building Material
		Grade : M-25

8	Test Result of Mix				
	Slump Achieved			85 mm	
	7 days compressive strength			22.9N/mm ²	
	28 days compressive strength			Awaited	
9	Mix proportion for 1m³ of concrete:				
	Water Content kg/m ³	Cement Content kg/m ³	Fine Aggregate kg/m ³	Coarse Aggregate, kg/m ³	
				10mm	20mm
	162.9	362	688	484	727
10	Ratio				
	0.45	1.0	1.900	1.337	2.008
11	Mix proportion for 50 kg of cement:				
	22.5	50.0	95.0	66.9	100.4

Note:

- 1 The above mentioned coarse and fine Aggregate are in saturated surface dry condition if dry aggregates are used, the amount of mixing water should be increased by an amount equal to the moisture likely to be absorbed by the aggregate.
- 2 If wet aggregates are used, necessary adjustments should be made on the mixing water and aggregates depending upon the amount of free (surface) moisture present.
- 3 It will be advisable to check the silt content of sand may require washing.
- 4 This mix design can be adopted at the site after carrying out trial, as usual.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001: 2015

+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwar, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**


Page 1 to 1

Report No.	HSL250820:27	Discipline :	Mechanical Testing
Sample Type	Aggregate	Group :	Building Material
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Grade/Size :	10mm
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Letter Date:	07/08/2025
Agreement No.	--	Sample Receipt Date	07/08/2025
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Start Date of Analysis	08/08/2025
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	End Date of Analysis	18/08/2025
Any Other Information	--	Date of Report Issue	18/08/2025

Sr. No.	Test Parameters	Units of Measurements	Results	Requirement as per IS: 383-2016	Method Reference
1	Sieve Analysis (Sieve Size)	% passing			IS: 2386(P-1)-1963
	12.5mm	--	100	100	
	10.0mm	--	96.9	85 - 100	
	4.75mm	--	11.8	0 - 20	
	2.36mm	--	2.5	0 - 5	
2	Specific Gravity	--	2.64	Not Specified	IS: 2386(P-3)-1963
3	Compacted Bulk Density	kg/ltr.	1.66	Not Specified	IS: 2386(P-3)-1963
4	Water Absorption	%	0.58	Not Specified	IS: 2386(P-3)-1963
5	Combined Flakiness & Elongation Index	%	31.8	40 Max.	IS: 2386(P-1)-1963
6	Deleterious Material				
(i)	Clay & Lumps	%	0.33	1.00 Max.	IS: 2386(P-2)-1963
(ii)	Material Finer than 75µm IS Sieve	%	0.52	1.00 Max.	IS: 2386(P-1)-1963
(iii)	Total Deleterious Materials	%	0.85	2.00 Max.	--
7	Aggregate Impact Value	% by wt.	17.4	30/45 Max. (Wearing surface/ Non wearing surface)	IS: 2386(P-4)-1963
8	Aggregate Crushing Value	% by wt.	22.6	30 Max. for Wearing surface	IS: 2386(P-4)-1963
9	Load Required for 10% Fine Value	KN	146	50 Min. for Non wearing Surface	IS: 2386(P-4)-1963

Statement of conformity as per lab decision rules: The sample conforms to IS: 383-2016 w.r.to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**


Page 1 to 1

Report No.	HSL250820:28	Discipline :	Mechanical Testing
Sample Type	Aggregate	Group :	Building Material
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Grade/Size :	20mm
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Letter Date:	07/08/2025
Agreement No.	--	Sample Receipt Date	07/08/2025
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Start Date of Analysis	08/08/2025
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर मे 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	End Date of Analysis	18/08/2025
Any Other Information	--	Date of Report Issue	18/08/2025

Sr. No.	Test Parameters	Units of Measurements	Results	Requirement as per IS: 383-2016	Method Reference
1	Sieve Analysis (Sieve Size)	% passing			IS: 2386(P-1)-1963
	40.0mm	%	100	100	
	20.0mm	%	96.5	85 - 100	
	10.0mm	%	4.0	0 - 20	
	4.75mm	%	0.6	0 - 5	
2	Specific Gravity	--	2.70	Not Specified	IS: 2386(P-3)-1963
3	Compacted Bulk Density	kg/ltr.	1.69	Not Specified	IS: 2386(P-3)-1963
4	Water Absorption	%	0.54	Not Specified	IS: 2386(P-3)-1963
5	Combined Flakiness & Elongation Index	%	31.2	40 Max.	IS: 2386(P-1)-1963
6	Deleterious Material				
(i)	Clay & Lumps	%	0.16	1.00 Max.	IS: 2386(P-2)-1963
(ii)	Material Finer than 75µm IS Sieve	%	0.34	1.00 Max.	IS: 2386(P-1)-1963
(iii)	Total Deleterious Materials	%	0.50	2.00 Max.	--
7	Aggregate Impact Value	% by wt.	18.9	30/45 Max.(Wearing surface/ Non wearing surface)	IS: 2386(P-4)-1963
8	Aggregate Crushing Value	% by wt.	23.1	30 Max. for Wearing surface	IS: 2386(P-4)-1963
9	Load Required for 10% Fine Value	KN	150	50 Min. for Non wearing Surface	IS: 2386(P-4)-1963

Statement of conformity as per lab decision rules: The sample conforms to IS: 383-2016 w.r.to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.



ISO 9001 : 2015

+91-9717912735

HS LABS PVT. LTD.An ISO 9001:2015 Certified Company
(A Govt. Approved Laboratory)Laboratory Address: Plot 576, Loni Road Near Naagdwara, Mohan Nagar Ghaziabad (UP)-201007
Regd. Off.: D-17/573 East Gokulpur Amar Colony Delhi-110094 E-Mail ID: hslabs83@gmail.com,
Phone Number: +91-9355465550, +91-9718202047, +91-9818187550, +91-9355275550,**TEST REPORT**


Page 1 to 1

Report No.	HSL250820:29	Discipline	: Mechanical Testing
Sample Type	Coarse Sand	Group	: Building Material
Name and Address of Customer	सहायक अभियन्ता यू०पी०आर०एन०एस०एस० निर्माण प्रखण्ड, ए-37 पुराना आवास विकास दिल्ली रोड, सहारनपुर	Grade/Size	: --
Reference No.	203 / यू०पी०आर०एन०एस०एस० / निप्रस / 2025-26	Letter Date:	07/08/2025
Agreement No.	--	Sample Receipt Date	07/08/2025
Name of Agency	मै० वसीम अहमद प्रो० श्री वसीम अहमद	Start Date of Analysis	08/08/2025
Name of Work/Subject	स्पर्श राजकीय दृष्टिबाधित बालिका विद्यालय, रामपुर मनिहारन जनपद सहारनपुर से 75 बेडेड बालिका छात्रा वास के निर्माण कार्य।	End Date of Analysis	18/08/2025
Any Other Information	--	Date of Report Issue	18/08/2025

Sr. No.	Test Parameters	Units of Measurements	Results	Requirement as per IS: 383-2016	Method Reference
1	Sieve Analysis (Sieve size)	% passing		Zone-II	IS: 2386(P-1)-1963
	10mm	-	100	100	
	4.75mm	-	95.0	90 - 100	
	2.36mm	-	82.2	75 - 100	
	1.18mm	-	61.6	55 - 90	
	600micron	-	41.2	35 - 59	
	300micron	-	24.6	8 - 30	
	150micron	-	7.2	0 - 10	
2	Specific Gravity	-	2.61	--	IS: 2386(P-3)-1963
3	Compact Bulk Density	Kg/ltr.	1.80	--	IS: 2386(P-3)-1963
4	Water Absorption	% by wt.	1.24	--	IS: 2386(P-3)-1963
5	Deleterious Material				
(i)	Clay & Lumps	%	0.69	1.00 Max.	IS: 2386(P-2)-1963
(ii)	Material Finer than 75µm IS Sieve	%	1.60	3.00 Max.	IS: 2386(P-1)-1963
(iii)	Total Deleterious Materials	%	2.29	4.00 Max.	--
6	Silt Content	% by volume	4.18	8 Max.	CPWD Specification
7	Fineness Modulus	%	2.88	--	IS: 2386(P-1)-1963
8	Organic Impurities	-	Passes the test	The colour of the liquid above the sand shall not be darker than a standard solution of tannic acid (2.5ml of 2% solution of tannic acid in 10% alcohol to 97.5ml of a 3% sodium hydroxide	IS: 2386(P-2)-1963

Statement of conformity as per lab decision rules: The sample conforms to IS: 383-2016 w.r.to the above tests.

End of Report



Terms & conditions: 1. Test reports are valid only for the sample tested in our laboratory. 2. Sample will be stored/kept in our stores for 90 days from the date of testing and shall be destroyed thereafter without any intimation. 3. Samples tested are Non-Returnable until specified at time of sample submission. 4. This report will not be valid for judicial purpose. 5. Total liability of our test house is limited to invoiced amount. 6. Result relate only to the item tested. 7. Report Shall not be reproduced without approval of the laboratory.

PROPOSED CONSTRUCTION OF
75 BEDD GIRLS HOSTEL FOR SPARSH
AT RAMPUR MANIHARAN DISTT
SAHARANPUR

Construction Agency:
U. P. R. N. S. S.
Office Of:
SARANPUR
CENTER LINE PLAN

ARCHITECT SIGN:
EXECUTIVE
ENGINEER

Job no.
Date
APRIL 2024

Dwg no.
RF-10
NORTH

Approved Consultant
DESIGN SQUARE
101, 102, 103, 104, 105, 106, 107, 108, 109, 110, 111, 112, 113, 114, 115, 116, 117, 118, 119, 120, 121, 122, 123, 124, 125, 126, 127, 128, 129, 130, 131, 132, 133, 134, 135, 136, 137, 138, 139, 140, 141, 142, 143, 144, 145, 146, 147, 148, 149, 150, 151, 152, 153, 154, 155, 156, 157, 158, 159, 160, 161, 162, 163, 164, 165, 166, 167, 168, 169, 170, 171, 172, 173, 174, 175, 176, 177, 178, 179, 180, 181, 182, 183, 184, 185, 186, 187, 188, 189, 190, 191, 192, 193, 194, 195, 196, 197, 198, 199, 200, 201, 202, 203, 204, 205, 206, 207, 208, 209, 210, 211, 212, 213, 214, 215, 216, 217, 218, 219, 220, 221, 222, 223, 224, 225, 226, 227, 228, 229, 230, 231, 232, 233, 234, 235, 236, 237, 238, 239, 240, 241, 242, 243, 244, 245, 246, 247, 248, 249, 250, 251, 252, 253, 254, 255, 256, 257, 258, 259, 260, 261, 262, 263, 264, 265, 266, 267, 268, 269, 270, 271, 272, 273, 274, 275, 276, 277, 278, 279, 280, 281, 282, 283, 284, 285, 286, 287, 288, 289, 290, 291, 292, 293, 294, 295, 296, 297, 298, 299, 300, 301, 302, 303, 304, 305, 306, 307, 308, 309, 310, 311, 312, 313, 314, 315, 316, 317, 318, 319, 320, 321, 322, 323, 324, 325, 326, 327, 328, 329, 330, 331, 332, 333, 334, 335, 336, 337, 338, 339, 340, 341, 342, 343, 344, 345, 346, 347, 348, 349, 350, 351, 352, 353, 354, 355, 356, 357, 358, 359, 360, 361, 362, 363, 364, 365, 366, 367, 368, 369, 370, 371, 372, 373, 374, 375, 376, 377, 378, 379, 380, 381, 382, 383, 384, 385, 386, 387, 388, 389, 390, 391, 392, 393, 394, 395, 396, 397, 398, 399, 400, 401, 402, 403, 404, 405, 406, 407, 408, 409, 410, 411, 412, 413, 414, 415, 416, 417, 418, 419, 420, 421, 422, 423, 424, 425, 426, 427, 428, 429, 430, 431, 432, 433, 434, 435, 436, 437, 438, 439, 440, 441, 442, 443, 444, 445, 446, 447, 448, 449, 450, 451, 452, 453, 454, 455, 456, 457, 458, 459, 460, 461, 462, 463, 464, 465, 466, 467, 468, 469, 470, 471, 472, 473, 474, 475, 476, 477, 478, 479, 480, 481, 482, 483, 484, 485, 486, 487, 488, 489, 490, 491, 492, 493, 494, 495, 496, 497, 498, 499, 500, 501, 502, 503, 504, 505, 506, 507, 508, 509, 510, 511, 512, 513, 514, 515, 516, 517, 518, 519, 520, 521, 522, 523, 524, 525, 526, 527, 528, 529, 530, 531, 532, 533, 534, 535, 536, 537, 538, 539, 540, 541, 542, 543, 544, 545, 546, 547, 548, 549, 550, 551, 552, 553, 554, 555, 556, 557, 558, 559, 560, 561, 562, 563, 564, 565, 566, 567, 568, 569, 570, 571, 572, 573, 574, 575, 576, 577, 578, 579, 580, 581, 582, 583, 584, 585, 586, 587, 588, 589, 590, 591, 592, 593, 594, 595, 596, 597, 598, 599, 600, 601, 602, 603, 604, 605, 606, 607, 608, 609, 610, 611, 612, 613, 614, 615, 616, 617, 618, 619, 620, 621, 622, 623, 624, 625, 626, 627, 628, 629, 630, 631, 632, 633, 634, 635, 636, 637, 638, 639, 640, 641, 642, 643, 644, 645, 646, 647, 648, 649, 650, 651, 652, 653, 654, 655, 656, 657, 658, 659, 660, 661, 662, 663, 664, 665, 666, 667, 668, 669, 670, 671, 672, 673, 674, 675, 676, 677, 678, 679, 680, 681, 682, 683, 684, 685, 686, 687, 688, 689, 690, 691, 692, 693, 694, 695, 696, 697, 698, 699, 700, 701, 702, 703, 704, 705, 706, 707, 708, 709, 710, 711, 712, 713, 714, 715, 716, 717, 718, 719, 720, 721, 722, 723, 724, 725, 726, 727, 728, 729, 730, 731, 732, 733, 734, 735, 736, 737, 738, 739, 740, 741, 742, 743, 744, 745, 746, 747, 748, 749, 750, 751, 752, 753, 754, 755, 756, 757, 758, 759, 760, 761, 762, 763, 764, 765, 766, 767, 768, 769, 770, 771, 772, 773, 774, 775, 776, 777, 778, 779, 780, 781, 782, 783, 784, 785, 786, 787, 788, 789, 790, 791, 792, 793, 794, 795, 796, 797, 798, 799, 800, 801, 802, 803, 804, 805, 806, 807, 808, 809, 810, 811, 812, 813, 814, 815, 816, 817, 818, 819, 820, 821, 822, 823, 824, 825, 826, 827, 828, 829, 830, 831, 832, 833, 834, 835, 836, 837, 838, 839, 840, 841, 842, 843, 844, 845, 846, 847, 848, 849, 850, 851, 852, 853, 854, 855, 856, 857, 858, 859, 860, 861, 862, 863, 864, 865, 866, 867, 868, 869, 870, 871, 872, 873, 874, 875, 876, 877, 878, 879, 880, 881, 882, 883, 884, 885, 886, 887, 888, 889, 890, 891, 892, 893, 894, 895, 896, 897, 898, 899, 900, 901, 902, 903, 904, 905, 906, 907, 908, 909, 910, 911, 912, 913, 914, 915, 916, 917, 918, 919, 920, 921, 922, 923, 924, 925, 926, 927, 928, 929, 930, 931, 932, 933, 934, 935, 936, 937, 938, 939, 940, 941, 942, 943, 944, 945, 946, 947, 948, 949, 950, 951, 952, 953, 954, 955, 956, 957, 958, 959, 960, 961, 962, 963, 964, 965, 966, 967, 968, 969, 970, 971, 972, 973, 974, 975, 976, 977, 978, 979, 980, 981, 982, 983, 984, 985, 986, 987, 988, 989, 990, 991, 992, 993, 994, 995, 996, 997, 998, 999, 1000

सुनील कुमार
आयुक्त
श्री ०० अर्थात् ००० ०००
प्रमाण प्रमाण प्रमाण

आयुक्त
श्री ०० अर्थात् ००० ०००
प्रमाण प्रमाण प्रमाण

सुनील कुमार
आयुक्त
श्री ०० अर्थात् ००० ०००
प्रमाण प्रमाण प्रमाण

